

SCoREBOARD

Triparty Collateral Management – H1 2021

French NSG





The Single Collateral Management Rulebook for Europe (SCoRE) contains 17 Standards related to triparty collateral management (published as the [AMI-SeCo Standards for Triparty Collateral Management](#)). Implementation progress is monitored twice per year. This summary report presents the results of the H1 2021 monitoring exercise conducted by the French NSG with the involvement of the following stakeholders:

There are two TPAs monitored in the French market

- 2 TPAs – BNP Paribas and Euroclear France

The SCoRE Overview provides a high-level summary of the H1 2021 monitoring exercise.

SCoRE Overview

SCoRE SINGLE COLLATERAL MANAGEMENT RULEBOOK FOR EUROPE	 Response Rate	 Implementation Status	 Milestones achieved?	 Implemented on Time?
TPA - BNP Paribas	100%	Implemented 11.4% Analysis started 77.1% Implementation started 0%	Yes	Yes
TPA - Euroclear France	100%	Implemented 8.57% Analysis started 0% Implementation started 40%	Yes	Yes

Note: Implemented on Time reflects the entity's expected ability to achieve the final milestone on time.

This NSG summary report is structured as follows: The Executive Summary provides an overview of the responses. Section 1 presents the compliance status of each entity type. Section 2 provides an overview of the progress against the individual milestones. Section 3 then provides a more detailed overview of the implementation status per Standard for each entity type.

Executive Summary

The two reporting entities fully responded to the survey in a timely manner. The French NSG secretariat continues its close follow-up on triparty standards for the months to come.

Implementation of the Triparty Collateral Management Standards in the French Market is not fully on track

This section presents the key findings of the survey for each entity type.

TPA – BNP Paribas

BNP Paribas (BNPP) has fully completed the monitoring survey in a timely manner. 11.1% of the TPA standards have already been implemented, while the analysis has started for the remaining 77.1%. Out of the 17 standards gathered in the SCoREBOARD, 4 have been implemented (blue) and 11 are on schedule for implementation (green). The 2 remaining standards are deemed non-applicable to BNPP. In addition, BNPP expects to meet all the next implementation milestones on time.

BNP Paribas implementation is on schedule. This entity expects to meet all dates of future implementation milestones by November 2023.

As a result, there is no issue of concern for BNPP, which should be fully compliant with the standards by November 2023.

TPA – Euroclear France

Euroclear France has completed the monitoring survey in a timely manner. 8.57% of the TPA standards have already been implemented and implementation has started for 40% of the standards. In its April 2021 adaptation plan, Euroclear France writes that adaptations are still required to support (1) the new ISO 20022 messaging format for Triparty collateral management, (2) the exchange of reference data between the ECMS and Euroclear France acting as TPA, and (3) certain Triparty processes specific to central banks.

Euroclear France is not on track to complete the implementation milestones, compliance with the Single Triparty Model will be achieved after November 2023.

Out of the 17 standards gathered in the SCoREBOARD, 3 have been implemented (blue), 12 are on schedule for implementation (green: ISO messaging and reference data) and 2 are not on schedule (yellow). In the commentary section of the questionnaire, Euroclear France explains its decision to prioritise all the necessary adaptations to secure the continuity of the Floating Collateral Management service by November 2023. Once these adaptations are complete, Euroclear will proceed with the implementation of the Single Triparty Collateral Management model. Full compliance with these standards will however only be achieved after the timeframe envisaged by the AMI-SeCo (November 2023).

CCPs

LCH SA, the French CCP, has not already started adaptations to relevant triparty standards

CCPs are monitored in their role as users of Triparty Collateral Management Services. As such, they are assessed on their ability to communicate with their TPAs using ISO 20022 messaging. Hence, in 2021, the Banque de France Oversight division questioned LCH SA regarding its expected adaptation to the ISO 20022 messaging format. While LCH SA is aware of the existence of triparty standards and has initiated talks with Euroclear France on the topic, the CCP confirmed that it has not yet started the related adaptations in 2021.

NCB

Banque de France will adopt the Single Triparty Model in November 2023,

Banque de France is on track to implement the AMI-SeCo standards for Triparty Collateral Management by November 2023.

SCoREBOARD

This section presents the overall compliance status in the market. TPAs are monitored on an individual basis and are assigned a colour-code status in accordance with the methodology outlined in Box 1¹.

Box 1

SCoREBOARD – Implementation Phase



SINGLE COLLATERAL MANAGEMENT RULEBOOK
FOR EUROPE

- The Standard has been implemented
 - Implementation of the Standard is on schedule (based on the agreed milestones)
 - Implementation is behind schedule (based on the agreed milestones)
 - Implementation has not started
-

Notes N/A

¹ For further details please refer to the [AMI-SeCo Monitoring Framework](#)

Table A
SCoREBOARD

STANDARD	TPA - BNP Paribas	TPA - Euroclear France
1: ISO 20022 messaging	G	Y
2: Initiation	G	G
3: Increase	G	G
4: Decrease	G	G
5: Revaluation	G	G
6: Cancellation	G	G
7: Unilateral removal	G	G
8: Reporting on flows	G	Y
9: Reporting on stocks	G	G
10: Closure	G	G
11: Handling of CA	N/A	G
12: Partial settlement	B	B
13: Reference data	G	G
14: Usage of baskets	B	B
15: Future dated	B	B
16: Operating hours	B	G
17: Cut-off Times Rule 1	N/A	G
17: Cut-off Times Rule 2	N/A	G
17: Cut-off Times Rule 3	N/A	G

Notes:

- For TPAs the colour-code reflects the current implementation status of each Standard in accordance with the methodology outlined in Box 1 above.
- A plausibility check was performed by the CMH-TF Secretariat.

2 Milestones

This section tracks an entity's progress in implementing the Standards on an ongoing basis. 13 milestones have been defined as listed in the box below.

Box 2 SCoRE Milestones

Milestone	Description	Date
M1	Analysis Started: Have you commenced an in-depth analysis of all applicable SCoRE Standards in order to identify and document all the changes required to internal processes and procedures in order to comply with the SCoRE Standards?	30/06/2020
M2	Initial Communication: Has initial high-level communication with external stakeholders on the changes introduced by SCoRE commenced?	01/03/2021
M3	Analysis Completed: Have you completed an in-depth analysis of all applicable SCoRE Standards?	31/07/2021
M4	Documentation Completed: Have you documented all the internal processes and procedures which need to be adapted in order to comply with the SCoRE Standards?	31/12/2021
M5	Detailed External Communication: Has detailed communication started regarding (i) upcoming changes in business processes, (ii) messaging formats and usage guidelines (in the case of new messages based on non-registered latest drafts by SWIFT) and (iii) planned testing activities been provided to users?	31/12/2021
M6	SCoRE Adaptation Started: Have you started to adapt/develop the processes and procedures in order to comply with the SCoRE Standards?	01/01/2022
M7	SCoRE Adaptation Complete: Have you completed the necessary adaptations/developments for the processes and procedures in order to comply with the SCoRE Standards?	30/06/2022
M8	Internal Testing Started for SCoRE: Have you started to test the changes to your internal processes and procedures which have been introduced in order to comply with the SCoRE Standards?	01/07/2022
M9	Internal Testing Complete for SCoRE: Have you completed the necessary internal testing?	02/12/2022
M10	External Testing Started for SCoRE: Are you in a position to test the changes introduced in order to comply with the SCoRE Standards with your user community (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	05/12/2022
M11	Final External Communication on SCoRE: has final communication to users been provided (i.e. updated user guide to reflect the changes implemented, final message usage guidelines for A2A communication) related to the SCoRE Standards?	01/04/2023
M12	External Testing Completed for SCoRE: Is the testing of the changes introduced in order to comply with the SCoRE Standards with your user community completed (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	13/10/2023
M13	SCoRE Standards Implemented: have the SCoRE Standards been implemented?	20/11/2023

Notes: N/A

Milestones expected to be achieved in the current reporting period are highlighted in blue in the header of Table B below. The blue colour-code is then assigned to those milestones which have been successfully achieved to date for each respective entity. Milestones which will only be achieved later are assigned a yellow status, while milestones which will only be achieved with significant delays / where work has not yet commenced are marked in red.

For the remaining milestones (i.e. milestones due to be achieved only after the current reporting cycle) the colour-code indicates an entity's expected ability to achieve a future milestone on time. The expected date of achievement is also indicated in the table if it is different to the milestone date defined by AMI-SeCo.

Table B
Milestones

	TPA - BNP Paribas	TPA - Euroclear France
Milestone 1 June 2020	Yes	Yes
Milestone 2 March 2021	Yes	Yes
Milestone 3 July 2021	Yes	Yes
Milestone 4 December 2021	Yes	Yes
Milestone 5 December 2021	Yes	Yes
Milestone 6 January 2022	Yes	Yes
Milestone 7 June 2022	Yes	Yes
Milestone 8 July 2022	Yes	Yes
Milestone 9 December 2022	Yes	06/22
Milestone 10 December 2022	Yes	Yes
Milestone 11 April 2023	Yes	Yes
Milestone 12 October 2023	Yes	Yes
Milestone 13 November 2023	Yes	Yes

Notes: Actors were asked to report for all milestones, i.e. whether they meet the current milestones and whether they expect to meet the dates for future milestones.

Summary

BNP Paribas expects to be on schedule for the 13 implementation milestones, while Euroclear France expects to meet the last milestones after the timeframe envisaged by the AMI-SeCo.


3

Implementation status per AMI-SeCo Standard

This section presents the implementation status of each Standard.

TPA - BNP Paribas

Implementation status per AMI-SeCo Standard

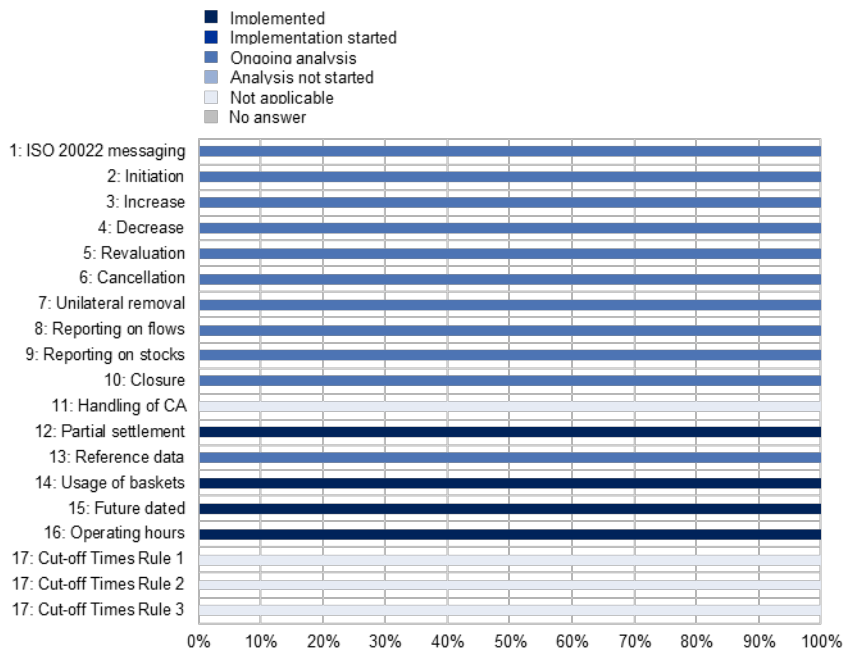


Notes

A plausibility check was performed by the CMH-TF Secretariat.

TPA - Euroclear France

Implementation status per AMI-SeCo Standard

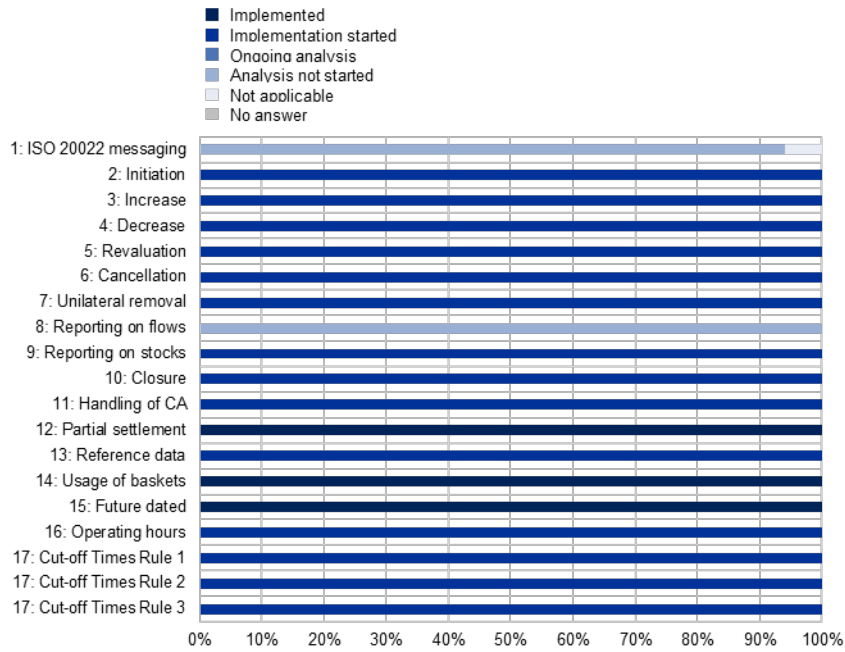

Notes

A plausibility check was performed by the CMH-TF Secretariat.

© European Central Bank, 2021

Postal address 60640 Frankfurt am Main, Germany
 Telephone +49 69 1344 0
 Website www.ecb.europa.eu

All rights reserved. Reproduction for educational and non-commercial purposes is permitted provided that the source is acknowledged.

The cut-off date for the data included in this report was 21 May 2021.

For specific terminology please refer to the [ECB glossary](#) (available in English only).
