

SCoREBOARD

Triparty Collateral Management – H2 2021






Belgian NSG

The Single Collateral Management Rulebook for Europe (SCoRE) contains 17 Standards related to triparty collateral management (published as the [SCoRE Standards for Triparty Collateral Management](#)). Implementation progress is monitored twice per year. This summary report presents the results of the H2 2021 monitoring exercise conducted by the Belgian NSG with the involvement of the following stakeholders:

There are two TPAs monitored in the Belgian market

- 2 TPAs – BNY Mellon and Euroclear Bank

SCoRE Overview

 <small>SINGLE COLLATERAL MANAGEMENT RULEBOOK FOR EUROPE</small>	 Response Rate	 Implementation Status	 Are all past milestones achieved?	 Implemented on Time?
TPA - BNY Mellon	100%	Implemented 7.69% Analysis started 61.5% Implementation started 26.9% Analysis not started 3.84%	No	Yes
TPA - Euroclear Bank	100%	Implemented 8.57% Analysis started 65.7% Implementation started 25.7% Analysis not started 0%	No	No

Note: Implemented on Time reflects the entity's expected ability to achieve the final milestone on time.

This NSG summary report is structured as follows: The Executive Summary provides an overview of the responses Section 1 presents the compliance status. Section 2 then provides an overview of the progress against the individual milestones.

Executive Summary

Implementation of the Triparty Collateral Management Standards in the Belgian market is partly on track

Implementation of the Triparty Collateral Management Standards in the Belgian market is partly on track. One of the two TPAs, namely BNY Mellon, is on track to adopt the Single Triparty Model in accordance with the implementation deadline agreed by AMI-SeCo. As of November 2023, Euroclear Bank will no longer meet the

criteria to remain a Eurosystem eligible TPA. This has an impact on the relevance of and compliance with some of the SCoRE Standards.

All reporting entities active in the Belgian market responded to the survey. This section presents the key findings of the survey for each entity type.

TPA – BNY Mellon

BNY Mellon implementation is partly on schedule

14 Standards related to triparty collateral management are applicable to BNY Mellon. 2 of these Standards have already been implemented (blue). For 7 Standards implementation has started (green). There are currently 5 Standards still under analysis. Since analysis should have been finalised by July 2021, its implementation is deemed to be behind schedule (yellow status).

BNY Mellon confirmed that it has met milestones 1 and 2. Since the analysis phase is taking more time than foreseen, milestone 3 has not been met and delays can be expected in several future milestones. Nevertheless, BNY Mellon will implement all applicable Standards by November 2023.

TPA – Euroclear Bank

Euroclear Bank implementation is partly on schedule

All Standards related to triparty collateral management are applicable to Euroclear Bank, in its capacity as a Eurosystem eligible TPA. 3 Standards have already been implemented (blue). Implementation of the ISO 20022 messaging Standard and reference data Standard has started (green).

Milestones 1 and 2 have been met. However, since the analysis of multiple standards is still ongoing, milestone 3 has not been met. Furthermore, Euroclear Bank should clarify all future milestones, following its announcement to implement the standards after joining T2S.

CCPs

CCPs are monitored in their role as users of Triparty Collateral Management Service

There are no CCPs that are active in the Belgian market in scope of this monitoring exercise.

NCB

NBB will adopt the Single Triparty Model in November 2023

The National Bank of Belgium is on track to implement the SCoRE Standards for Triparty Collateral Management by November 2023, provided that the ECMS project remains on track.

SCoREBOARD

This section presents the overall compliance status in the market. TPAs are monitored on an individual basis and are assigned a colour-code status in accordance with the methodology outlined in Box 1¹.

Box 1

SCoREBOARD – Implementation Phase



SINGLE COLLATERAL MANAGEMENT RULEBOOK
FOR EUROPE

- The Standard has been implemented
- Implementation of the Standard is on schedule (based on the agreed milestones)
- Implementation is behind schedule (based on the agreed milestones)
- Implementation has not started

Notes: N/A

¹ For further details please refer to the [AMI-SeCo Monitoring Framework](#)

Table A
SCoREBOARD

STANDARD	TPA - BNY Mellon	TPA - Euroclear Bank
1: ISO 20022 messaging	Y	Y
2: Initiation	G	Y
3: Increase	G	Y
4: Decrease	G	Y
5: Revaluation	G	Y
6: Cancellation	G	Y
7: Unilateral removal	Y	Y
8: Reporting on flows	Y	Y
9: Reporting on stocks	G	Y
10: Closure	G	Y
11: Handling of CA	N/A	Y
12: Partial settlement	B	B
13: Reference data	Y	G
14: Usage of baskets	B	B
15: Future dated	Y	B
16: Operating hours	N/A	Y
17: Cut-off Times Rule 1	N/A	Y
17: Cut-off Times Rule 2	N/A	Y
17: Cut-off Times Rule 3	N/A	Y
17: Cut-off Times Rule 4	N/A	Y

Notes:

- For TPAs the colour-code reflects the current implementation status of each Standard in accordance with the methodology outlined in Box 1 above.
- A plausibility check was performed by the CMH-TF Secretariat.

2 Milestones

This section tracks an entity's progress in implementing the Standards on an ongoing basis. 13 milestones have been defined as listed in the box below.

Box 2 SCoRE Milestones

Milestone	Description	Date
M1	Analysis Started: Have you commenced an in-depth analysis of all applicable SCoRE Standards in order to identify and document all the changes required to internal processes and procedures in order to comply with the SCoRE Standards?	30/06/2020
M2	Initial Communication: Has initial high-level communication with external stakeholders on the changes introduced by SCoRE commenced?	01/03/2021
M3	Analysis Completed: Have you completed an in-depth analysis of all applicable SCoRE Standards?	31/07/2021
M4	Documentation Completed: Have you documented all the internal processes and procedures which need to be adapted in order to comply with the SCoRE Standards?	31/12/2021
M5	Detailed External Communication: Has detailed communication started regarding (i) upcoming changes in business processes, (ii) messaging formats and usage guidelines (in the case of new messages based on non-registered latest drafts by SWIFT) and (iii) planned testing activities been provided to users?	31/12/2021
M6	SCoRE Adaptation Started: Have you started to adapt/develop the processes and procedures in order to comply with the SCoRE Standards?	01/01/2022
M7	SCoRE Adaptation Complete: Have you completed the necessary adaptations/developments for the processes and procedures in order to comply with the SCoRE Standards?	30/06/2022
M8	Internal Testing Started for SCoRE: Have you started to test the changes to your internal processes and procedures which have been introduced in order to comply with the SCoRE Standards?	01/07/2022
M9	Internal Testing Complete for SCoRE: Have you completed the necessary internal testing?	02/12/2022
M10	External Testing Started for SCoRE: Are you in a position to test the changes introduced in order to comply with the SCoRE Standards with your user community (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	05/12/2022
M11	Final External Communication on SCoRE: has final communication to users been provided (i.e. updated user guide to reflect the changes implemented, final message usage guidelines for A2A communication) related to the SCoRE Standards?	01/04/2023
M12	External Testing Completed for SCoRE: Is the testing of the changes introduced in order to comply with the SCoRE Standards with your user community completed (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	13/10/2023
M13	SCoRE Standards Implemented: have the SCoRE Standards been implemented?	20/11/2023

Notes: N/A

Milestones expected to be achieved in the current reporting period are highlighted in blue in the header of Table B below. The blue colour-code is then assigned to those milestones which have been successfully achieved to date for each respective entity. Milestones which will only be achieved later are assigned a yellow status, while milestones which will only be achieved with significant delays / where work has not yet commenced are marked in red.

For the remaining milestones (i.e. milestones due to be achieved only after the current reporting cycle) the colour-code indicates an entity's expected ability to achieve a future milestone on time. The expected date of achievement is also indicated in the table if it is different to the milestone date defined by AMI-SeCo.

Table B
Milestones

	TPA - BNY Mellon	TPA - Euroclear Bank
Milestone 1 June 2020	Yes	No
Milestone 2 March 2021	Yes	No
Milestone 3 July 2021	11/22	No
Milestone 4 December 2021	11/22	No
Milestone 5 December 2021	12/22	No
Milestone 6 January 2022	Yes	No
Milestone 7 June 2022	09/23	No
Milestone 8 July 2022	Yes	No
Milestone 9 December 2022	10/23	06/22
Milestone 10 December 2022	10/23	No
Milestone 11 April 2023	10/23	No
Milestone 12 October 2023	11/23	No
Milestone 13 November 2023	Yes	No

Notes: Actors were asked to report for all milestones, i.e. whether they meet the current milestones and whether they expect to meet the dates for future milestones.

Summary

Both responding TPAs have reached the first two implementation milestones. BNY Mellon has not yet finalised its analysis (to be expected by November 2022) and is therefore facing delays in several (future) milestones. Nevertheless, all standards should be implemented by November 2023. Euroclear Bank expressed its intention to offer Triparty Collateral Management services under the Single Triparty Collateral Management model once it has migrated to T2S. It is therefore not expected to be fully compliant with the ISO 20022 messages by November 2023.


3

Implementation status per SCoRE Standard

This section presents the implementation status of each Standard.

BNY Mellon

Implementation status per SCoRE Standard

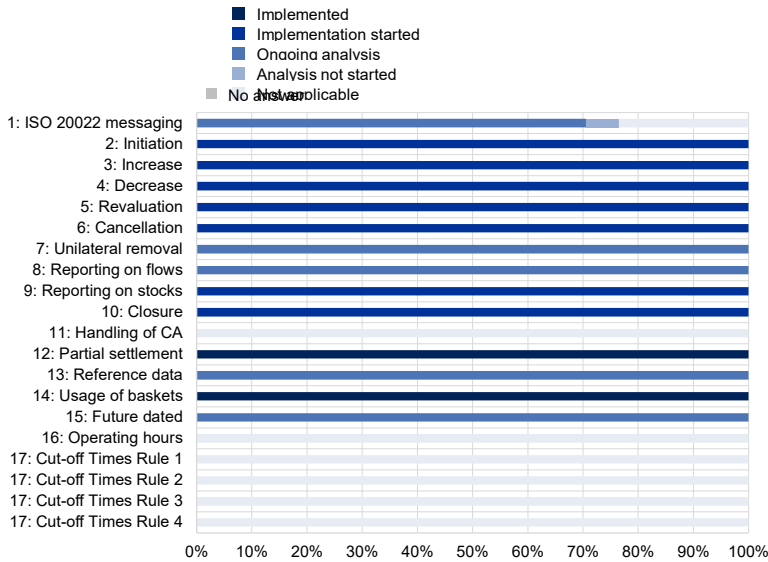


Notes

A plausibility check was performed by the CMH-TF Secretariat.

Euroclear Bank

Implementation status per SCoRE Standard

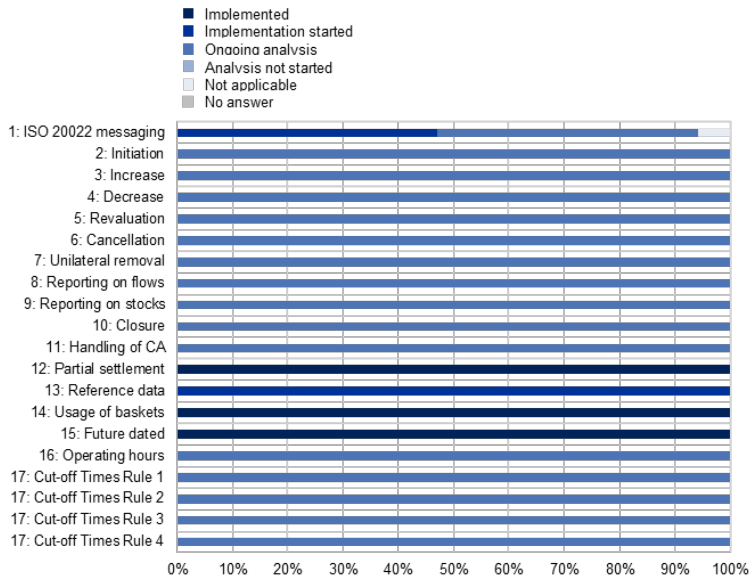

Notes

A plausibility check was performed by the CMH-TF Secretariat.

© **European Central Bank, 2022**

Postal address 60640 Frankfurt am Main, Germany

Telephone +49 69 1344 0

Website www.ecb.europa.eu

All rights reserved. Reproduction for educational and non-commercial purposes is permitted provided that the source is acknowledged.

The cut-off date for the data included in this report was 17 November 2021.

For specific terminology please refer to the [ECB glossary](#) (available in English only).
